IoT Calipers with Wireless Data Receiver for QC Inspection
DASHBOARD

GARUDA YAMATO STEEL

Project Objective

The project aims to digitize and streamline quality control processes by replacing manual recording with automated data capture, ensuring standardized procedures, and enabling real-time monitoring and traceability through a web-based dashboard. It is designed to enhance consistency, reduce risks, support historical data review, and remain future-ready with seamless integration into existing systems and emerging

Project Detail

Project Name	IoT Calipers with Wireless Data Receiver
Project Manager	Narintorn Seetanan & Rizal Al Deny
Target Start Date	02/06/25
Target End Date	15/01/26

Tasks by Status

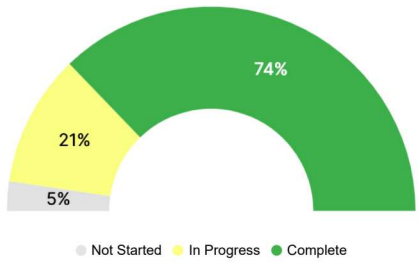

PR / PO Progress

Plan vs Actual Date

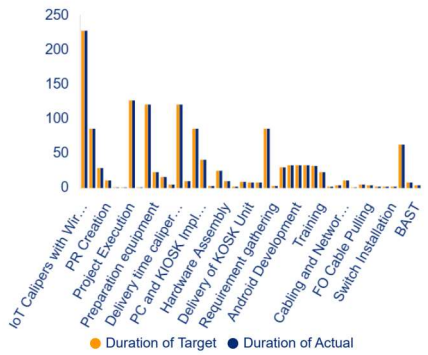

Project Progress

Progress Percentage

68%

Budget Summary

Budget Plan Total(USD)

$40.000,01

Budget Commitment Total(USD)

$15.350,95

Budget Actual Total(USD)

$13.187,62

Budget Overview

Project Milestones

Task Name	Start Date	End Date	% Complete	Status
IoT Calipers with Wireless Data Receiver	06/02/25	01/15/26	68%	In Progress
Administration	06/02/25	08/26/25	100%	Complete
Project Execution	09/02/25	01/06/26	70%	In Progress
Review	11/14/25	01/15/26	20%	In Progress

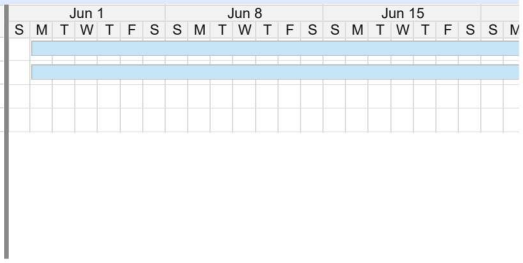

Overdue Tasks

Task Name	Assigned To	Start Date	End Date	% Complete

In Progress Task

Task Name	Assigned To	Start Date	End Date	% Complete
UAT	Rizal Al Deny, Muhan	11/20/25	11/21/25	25%
Baby sitting & documentation	Rizal Al Deny, Muhan	11/14/25	11/21/25	30%
Software development	Rizal Al Deny	09/10/25	12/04/25	97%

Not Started

Task Name	Assigned To	Start Date	End Date	% Complete
Go Live	Rizal Al Deny, Muhan	12/01/25	12/04/25	0%

BAST	Rizal Al Deny, Muhan	01/12/26	01/15/26	0%

Picture Update

FO Pulling, UTP, Switch Installation

Cable FO and UTP already terminated in BP1 & LSM

Switch in BP1 Cooling bed & LSM already Active

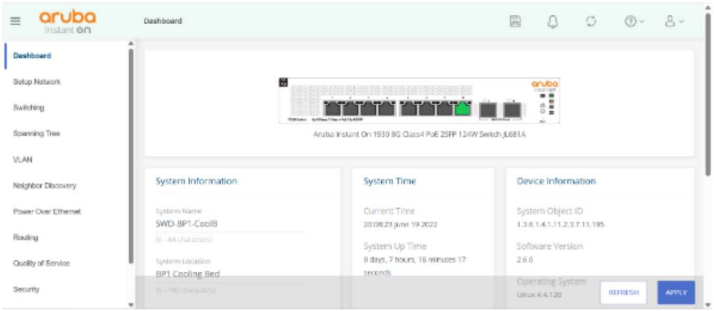

UI UX Software Design For Web already completed

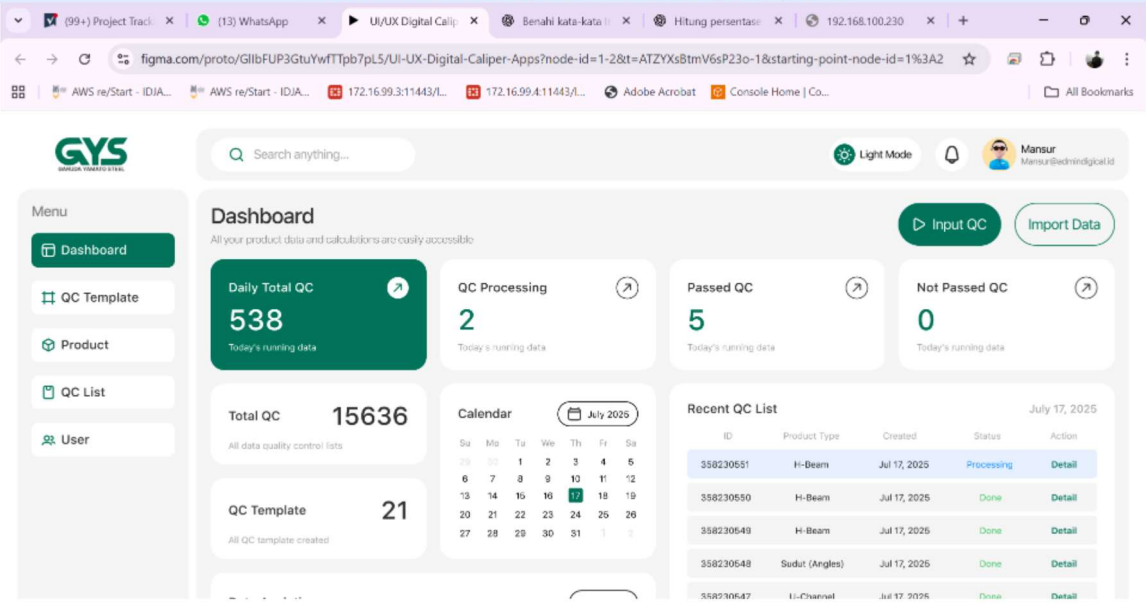

Server Environment



UI/UX Discussion



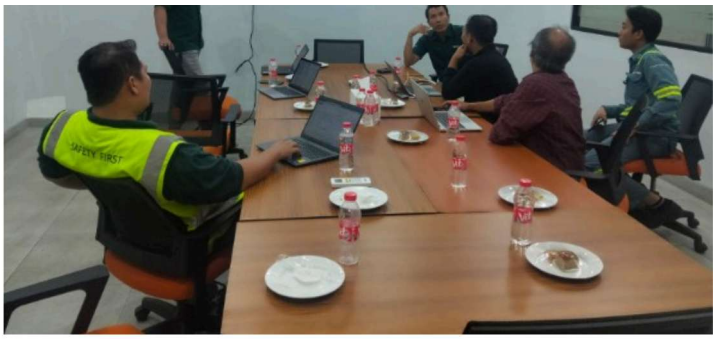

The kiosk setup has been completed at CB2

Kiosk setup has been completed at CB1

Testing Digital Caliper with application Software

Testing caliper with application software

Discuss for Application

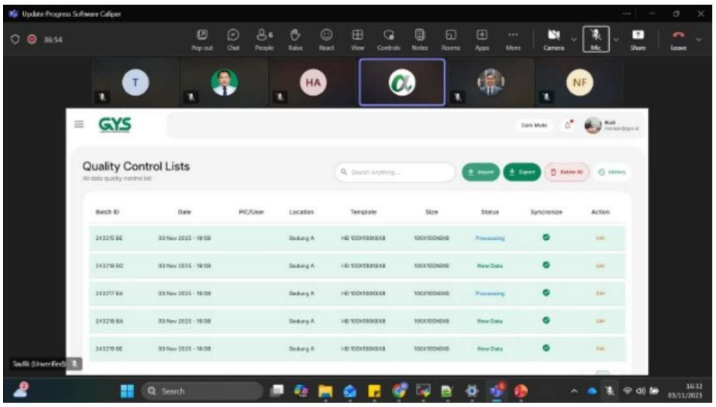

Sharedfolder from PPIC

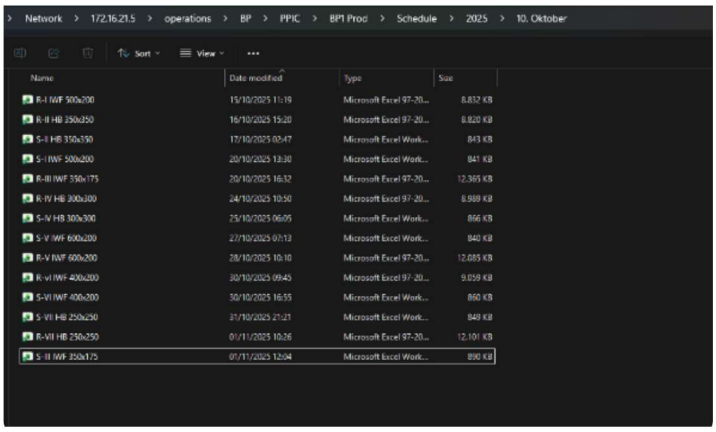

Connect software with sharingfolder



Software Process Deploy on Server GYS





Testing Bot Whatsapp

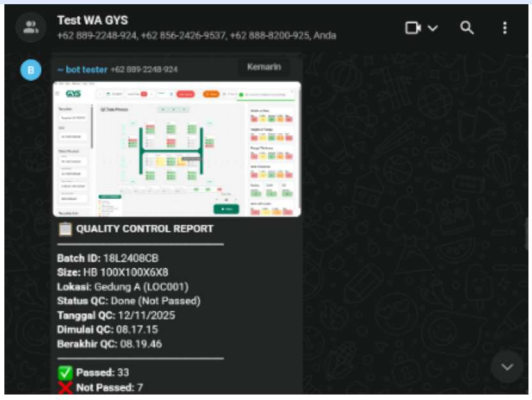

Training application on Cutting Room at BP1

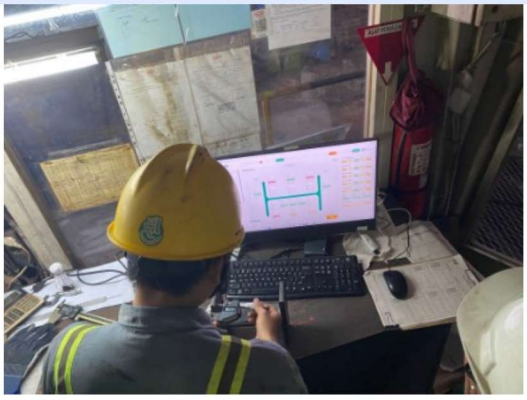

Key Updates

Issues

Progress & Accomplishment

- The kiosk PC cover has been installed.
- The soft go-live has been successfully completed.
- Training and UAT will begin on 20 November and will continue for 7 days.
- The application has been deployed to the GYS production server.
- The WhatsApp notification feature has also been successfully activated and is running properly.

Next Plan

- Ensure that the training and UAT sessions run smoothly.
- Verify that there are no remaining bugs, errors, or features that are still not aligned with the requirements.
- Once everything has been confirmed to be in good condition, the project can proceed to the final go-live.

Our Other Proud Project

Smartsheet Enhanchement

Project Tracking & Rollup

Hyperconverged Infrastructure

Project Tracking & Rollup

GYS Noble House Satelite Office Relocation

Project Tracking & Rollup

Timeline

Months

2025 2026

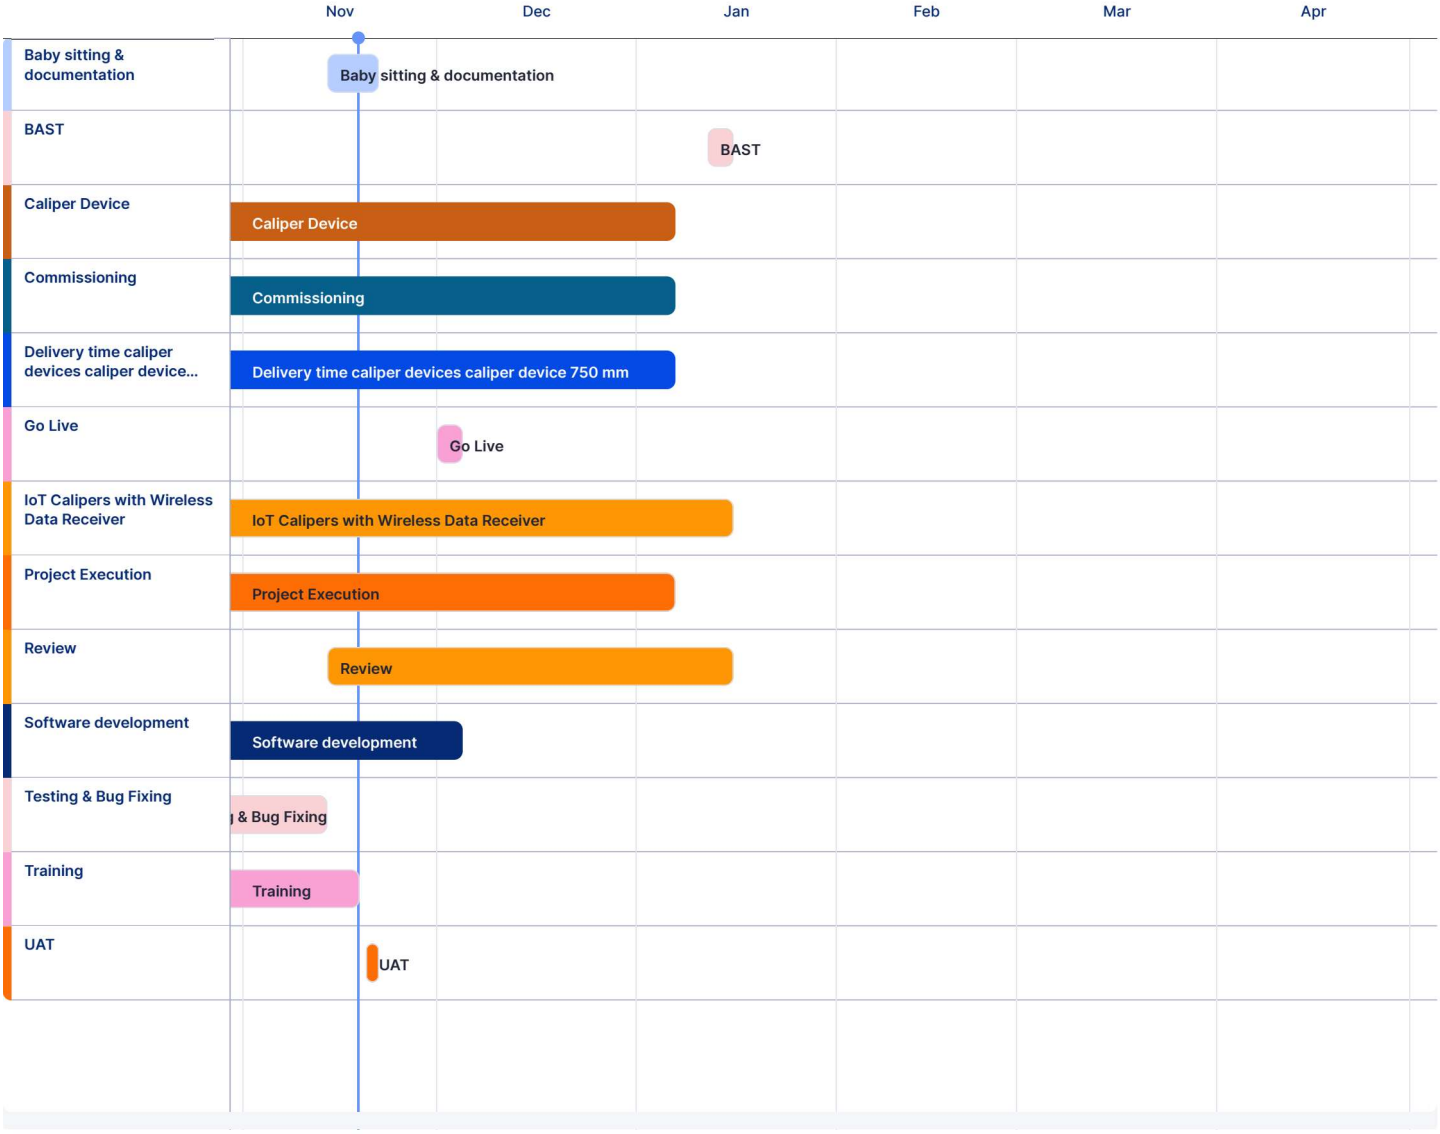
Nov
Dec
Jan
Feb
Mar
Apr
Baby sitting & documentation
Baby sitting & documentation
BAST
BAST
Caliper Device
Caliper Device
Commissioning
Commissioning
Delivery time caliper devices caliper device...
Delivery time caliper devices caliper device 750 mm
Go Live
Go Live
IoT Calipers with Wireless Data Receiver
IoT Calipers with Wireless Data Receiver
Project Execution
Project Execution
Review
Review
Software development
Software development
Testing & Bug Fixing
& Bug Fixing
Training
Training
UAT
UAT
